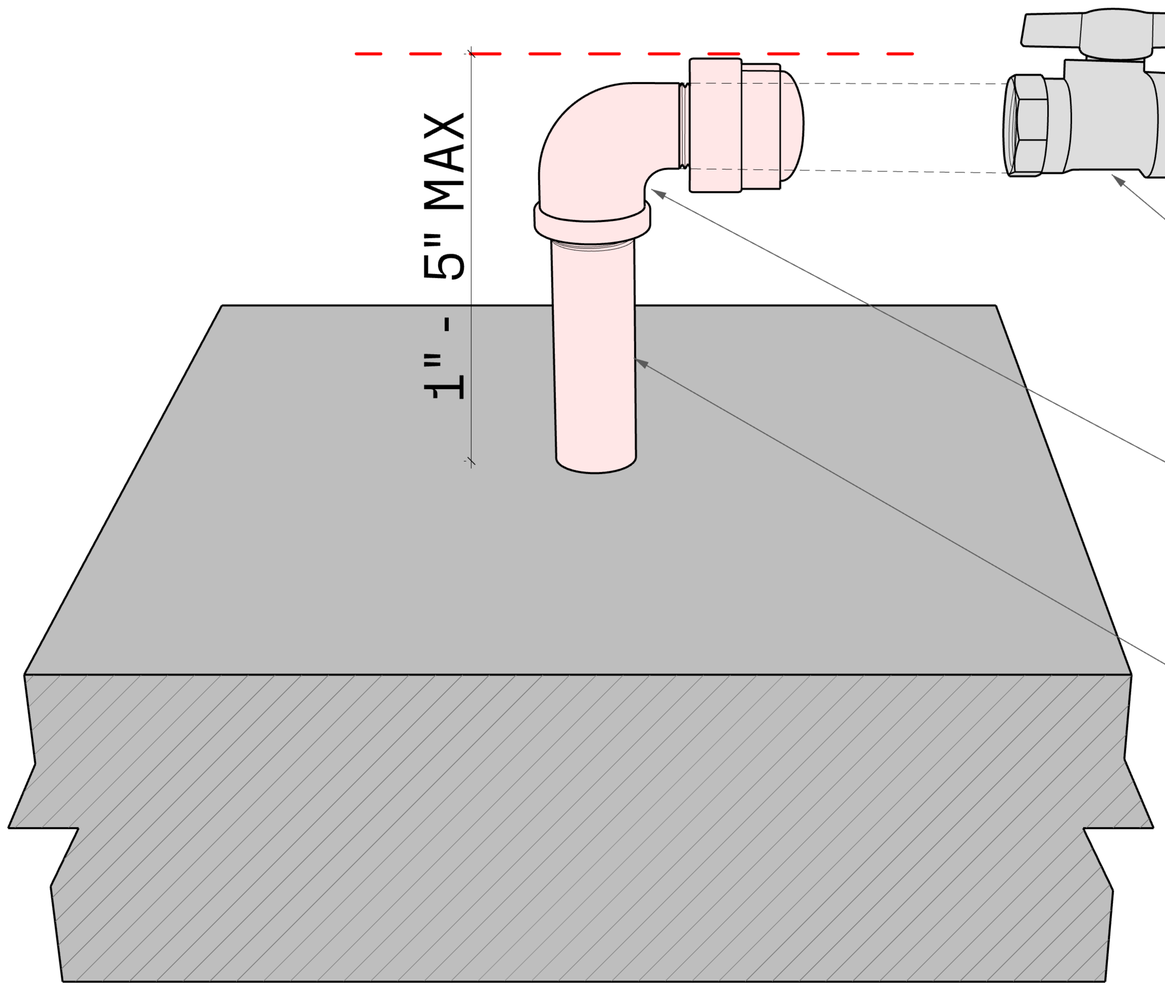

LUMACAST WHITE GLOVE SERVICE

White glove delivery is available for all manual ignition fire tables **ONLY**.

Electronic ignition **MUST** be installed by licensed contractor/electrician.

For successful installation, hardline stub up should be capped off between 1" and 5" off finished floor. The Lumacast team can provide and attached a 1/2" or 5/8" Flair Ball Valve shut off to the stub up and plum the fire table

1/2" OR 5/8" FLAIR BALL VALVE CAN BE SUPPLIED BY LUMACAST TEAM

HARDLINE STUB UP CAPPED OFF WITH SHUT OFF COMING FROM SUPPLY (HOUSE).

SEE PLUMBER FOR SIZING OF SUPPLY PIPE.

OUR TEAM CAN **ONLY INSTALL ON IPS PIPING**, PLASTIC PLUMBING MUST BE CONNECTED BY CONTRACTOR.

LUMACAST

7171 Ronson Rd
San Diego, CA 92111
t: +1 888 710 1026
www.lumacast.com

PROJECT INFROMATION

PROJECT:
LUMACAST FIRE-TABLE
- - -

DESIGNER:
LUMACAST

DRAWING INFORMATION

DRAWING PACKAGE:
2D SHOP DRAWINGS

SHEET CONTENTS:
COVER SHEET

COLOR:	- - -
INFILL:	- - -
IGNITION:	- - -
BURNER:	- - -
BTU:	- - -
GWT:	- - -
ALU TOP:	Y ☐ N ☐
A.W COVER:	Y ☐ N ☐
WIND GUARD:	Y ☐ N ☐

☐ PRELIMINARY / UNDER REVISION
☐ APPROVED FOR PRODUCTION

SIGN:

DATE:

AUTHOR	AUTHOR
EGI	11/21

P.02
SHEET NO

P.02 PLUMBING STUB UP DETAIL
